



Solid Waste Management Improvement Project

ADB Loan No.: 3067-UZB

**PROJECT MANAGEMENT, IMPLEMENTATION AND
SUPERVISION CONSULTANCY SERVICES**

Contract No.: SUE/Maxsustrans/QCBS-Cons_1-2016-01



Semi-Annual Social Safeguards Monitoring Report

Reporting period: January – June 2024

CLIENT – IMPLEMENTING AGENCY

State Unitary Enterprise (SUE) “MAXSUSTRANS” (Uzbekistan)

LEAD CONSULTANT

Infratech Consulting SDN Ltd. (Uzbekistan)



Semi-Annual Social Safeguard Monitoring Report

15th Semi-annual report for January – June 2024

Project No: 45366
ADB Loan 3067-UZB

Draft No. 1 (July 2024)

UZB: Solid Waste Management Improvement Project (SWMIP) financed by the ADB

Prepared by: PIU Consultants - Infratech Consulting SDN Ltd. (Uzbekistan)

For: State Unitary Enterprise «Maxsustrans», Khokimiyat of Tashkent City and ADB

Endorsed by: Mr. Jamoliddin Irbutayev – Acting Head of PIU

Abbreviations

ADB	-	Asian Development Bank
AH	-	Affected Household
AP	-	Affected Person
CAP	-	Correction Action Plan
EA	-	Executing Agency
GFP	-	Grievance Focal Point
GOU	-	Government of Uzbekistan
GRM	-	Grievance Redress Mechanism
Ha	-	Hectare
IA	-	Implementing Agency
IR	-	Involuntary Resettlement
IWP	-	Informal Waste Picker
LARP	-	Land Acquisition and Resettlement Plan
MOF	-	Ministry of Finance
MSW	-	Municipal Solid Waste
O&M	-	Operation and Maintenance
PIU	-	Project Implementation Unit
PPTA	-	Project Preparatory Technical Assistance
SLF	-	Sanitary Landfill
SSEMP	-	Social safeguard and Environmental Monitoring plan
SWM	-	Solid Waste Management

Glossary

Compensation	Payment in cash or kind for an asset to be acquired or affected by a project at replacement cost.
Affected Persons	Affected persons (APs) are those who experience full or partial, permanent or temporary physical displacement (relocation, loss of residential land, or loss of shelter) and economic displacement (loss of land, assets, access to assets, income sources, or means of livelihoods) resulting from (i) involuntary acquisition of land, or (ii) involuntary restrictions on land use or on access to legally designated parks and protected areas. APs could be of three types: (i) persons with formal legal rights to land lost in its entirety or in part; (ii) persons who lost the land they occupy in its entirety or in part who have no formal legal rights to such land, but who have claims to such lands that are recognized or recognizable under national laws; and (iii) persons who lost the land they occupy in its entirety or in part who have neither formal legal rights nor recognized or recognizable claims to such land.
Entitlement	The range of measures comprising cash or kind compensation, relocation cost, income rehabilitation assistance, transfer assistance, income substitution, and relocation which are due to /business restoration which are due to AH, depending on the type and degree nature of their losses, to restore their social and economic base. All entitlements will be given to all affected households as per the entitlement matrix.
Hokimiyat	Local government authority that interfaces between local communities and the government at the regional and national level. It has ultimate administrative and legal authority over local populations residing within its jurisdiction.
Land acquisition	The process whereby a person is compelled by a public agency to alienate all or part of the land s/he owns or possesses, to the ownership and possession of that agency, for public purposes, in return for fair compensation.
Mahalla	Is a local level community-based organization recognized official by the GoU that serves as the interface between state and community and is responsible for facilitating a range of social support facilities and ensuring the internal social and cultural cohesiveness of its members. Mahalla leaders are elected by their local communities.
Meaningful Consultation	A process that (i) begins early in the project preparation stage and is carried out on an ongoing basis throughout the project cycle; (ii) provides timely disclosure of relevant and adequate information that is understandable and readily accessible to affected people; (iii) is undertaken in an atmosphere free of intimidation or coercion; (iv) is gender inclusive and responsive, and tailored to the needs of disadvantaged and vulnerable groups; and (v) enables the incorporation of all relevant views of affected people and other

stakeholders into decision making, such as project design, mitigation measures, the sharing of development benefits and opportunities, and implementation issues.

Illegal	HHs that are not registered their business, agriculture, residential and orchard and those who have no recognizable rights or claims to the land that they are occupying and includes people using private or state land without permission, permit or grant i.e. those people without legal lease to land and/or structures occupied or used by them. ADB's policy explicitly states that such people are entitled to compensation for their non-land assets.
Replacement cost	Replacement cost is the principle to be complied with in compensating for lost assets. Calculation of which should include: (i) fair market value; (ii) transaction costs; (iii) interest accrued, (iv) transitional and restoration costs; and (v) other applicable payments, if any. Where market conditions are absent or in a formative stage, APs and host populations will be consulted to obtain adequate information about recent land transactions, land value by types, land titles, land use, cropping patterns and crop production, availability of land in the project area and region, and other related information. Baseline data on housing, house types, and construction materials will also be collected. Qualified and experienced experts will undertake the valuation of acquired assets. In applying this method of valuation, depreciation of structures and assets should not be taken into account.
Significant impact	200 people or more will experience major impacts, which are defined as; (i) being physically displaced from housing, or (ii) losing 10% or more of their productive assets (income generating).
Vulnerable Households	Low-income households, female-headed households with fewer than 2 adult income- earners, the elderly headed with unemployed family members, and disabled.
Leaseholder	Legal entity (registered farm) running agricultural production with the use of land plots granted to him on a long-term lease. Lease term is limited up to fifty years but not less than for ten years. Leaseholder cannot sell - buy, mortgage, sublease present, exchange the land.

Table of Content

Abbreviations	3
Glossary.....	4
1. Executive Summary	7
2. Introduction.....	10
3. Project Contracts and Management	11
4. Social Safeguard Activities during January – June 2024	13
4.1 Objectives of the report and methodology.....	13
4.2 Scope of Social Safeguard Monitoring Report.....	13
4.3 Project activities in January – June 2024	13
4.4 Project monitoring for the construction period	14
5. Redress Grievances	17
6. Public Awareness and Consultations.....	18
7. Conclusions.....	19

1. Executive Summary

1. **The Government of Uzbekistan (GoU)** has applied for a loan from the Asian Development Bank (ADB) for the development and improvement of Solid Waste Management (SWM) system of the capital city - Tashkent. ADB approved the project on 27 November 2013 with a loan amount of \$69.0 million from its ordinary capital resources. The loan reference number is L3067-UZB: Solid Waste Management Improvement Project (SWMIP). The Loan Agreement was signed between the Republic of Uzbekistan and ADB on 27 February 2014, and the Project Agreement was signed between ADB, Tashkent City Municipality and the SUE “Maxsustrans” on 12 March 2014. The Loan Agreement became effective on 29 December 2014 and comprises **Part A** – National Municipal Solid Waste Strategy and **Part B** – Solid Waste Management in Tashkent city.
2. **Solid Waste Management Improvement Project** was originally designed for five years of implementation with a loan closing date of 30 June 2019. On 17 December 2018, ADB approved a two-year loan extension with the revised Loan Closing Date of 30 June 2021 to complete all ongoing contracts and planned civil works, delayed due to start-up delays (including ten months’ delay in effectiveness) and procurement delays (the first contract was awarded in 2016 only) because of the Executing Agency’s insufficient capacity and GoU’s prolonged contract registration process.
3. **Loan extension (second request).** Based on the letters of the Ministry of Finance of Uzbekistan dated 26 March 2021 and 17 July 2021, on 23 July 2021, ADB approved a 30-months loan extension with the revised Loan Closing Date from 30 June 2021 to 31 December 2023 to ensure a successful completion of the landfill construction component. This approval was provided by ADB on a post-facto-basis considering the GoU’s commitment to strictly adhering to the time-bound action plan and mitigation measures submitted to ADB and to be implemented by Tashkent City Municipality, Maxsustrans, and PIU.
4. **Loan extension (third request).** On 18 September 2023, the Ministry of Economy and Finance requested for the third extension of the loan closing date, from 31 December 2023 to 31 December 2024. On 26 September 2023, the Maxsustrans provided additional justifications for the loan extension, citing delays in the landfill construction and insufficient time to complete the civil works by the end of 2023. The delays are due to (i) adverse weather conditions between November 2022 and March 2023, and (ii) design changes to the access road and cell three of the landfill because of higher groundwater level detected. ADB provided its approval on 25 December 2023 considering the GoU commitment to complete all remaining project activities within the extended timeframe.
5. **The overall objective of SWMIP** is to provide an improved SWM system in Tashkent, the capital city, to upgrade urban infrastructure and services. The project’s impact is improved urban environment and quality of life for the residents of Tashkent. The expected outcome is improved SWM services and management in Tashkent. The project has three outputs: **output 1** - rehabilitated and expanded SWM system in Tashkent; **output 2** - strengthened operational capacity; and **output 3** - national SWM strategy. Tashkent City Municipality is the Executing Agency for the outputs 1 and 2, with State Committee of Uzbekistan of Ecology and Environment Protection (SCEEP) being the Executing Agency for output 3. Maxsustrans is the Implementing Agency responsible for the day-to-day project implementation.
6. The total project cost is **\$76.3 million** equivalent (of which ADB loan \$69.0 million), inclusive of taxes and duties, benefits, and financial charges during implementation covered by the GoU.

The project finances:

- supply of garbage trucks for collection and transportation of household solid waste;
- supply of equipment and machinery for the sanitary landfill;
- supply of waste bins for waste collection points and containers for transportation of solid waste;
- rehabilitation of two transfer stations of Maxsustrans located in Tashkent;
- reconstruction of two garages of Maxsustrans located in Tashkent;
- construction of a new sanitary landfill in Akhangaran district of Tashkent region;
- preparation of a National strategy for the solid waste management, including a sector investment program;
- capacity development support for Maxsustrans, including in the areas of operation and management and Project implementation; and
- development and implementation of a waste minimization and recycling program and a parallel media and public awareness campaign about waste minimization and recycling.

7. **Construction and rehabilitation of waste collection points** was financed by Maxsustrans's own funds and **Closure of existing dumpsite** is financed by funds of Sejin G&E Co. Ltd. Company (Republic of Korea) - for details please refer to the next chapter below. Therefore, these works components are no longer part of the Project.
8. **Social Safeguard Monitoring** is carried out to report any social concerns occurred during project implementation. Social safeguard monitoring is carried out for issues of land acquisition and involuntary resettlement in compliance with the ADB requirements. Initial background for the social safeguard monitoring is Land acquisition and resettlement plan (LARP) designed for the landfill area. This semiannual report on social safeguards monitoring is prepared to serve the purpose for compliance with ADB's safeguards on social safeguard issues that may occur during implementation of the project. This report covers the period of January – June 2024.
9. **Land Acquisition and Resettlement:** To assess the project impacts on land related to the construction of new landfill at the stage of Feasibility Study preparation within the project the land acquisition and resettlement plan was designed in 2012. In compliance with the ADB requirements the LARP must be updated at the stage of detailed project design. The project category was specified as Category B. In October 2019 the detailed design of the SLF project was prepared and approved by local authority. However, regular Social safeguard monitoring showed that the project does not involve the involuntary land acquisition and resettlement impacts. As a part of social safeguard monitoring Due Diligence was conducted and approved by ADB in October 2019. Due Diligence confirmed that there are no the involuntary land acquisition and resettlement impacts within the project. In compliance with the request of ADB Due Diligence was updated in April 2020 and included more detailed clarification on land acquisition and resettlement impacts. The updated Due Diligence report was submitted to ADB's review in May 2020.
10. During the reporting period no construction activities of company Sejin G&E Co., Ltd on old dumpsite were observed. As reported in the previous monitoring report in accordance with the Order of the Khokimiyat of the Akhangaran region No. 3861 dated 15.06.2019 a land plot of 1 hectare for installation the biogas facility has been allocated to Sejin G&E Co., Ltd. This land plot is located on the dumpsite area and occupied by the administrative building of the landfill operating unit of SUE "Maxsustrans". There are no negative impacts on residents of nearby villages due to acquisition of this land.
11. **Gender:** Gender Action Plan for the reporting period is prepared and submitted to ADB by PIU.

12. **Redress Grievances:** Grievance redress mechanism is designed for the project in LARP 2012. The complaint handling process is reported to ADB through monitoring reports. The safeguard specialist of Project Supervision Consultant periodically reviews and records the efficiency and effectiveness of the GRM highlighting the project's ability to prevent and address grievances. During the monitoring period no complaints from the nearby residents and households were registered.
13. **Public Awareness and Consultations:** During the monitoring period, no public consultations were conducted. The earth works on the new landfill have been completed in 2023 and no public consultations and awareness have been required. In old dumpsite project of Sejin G&E Co., Ltd for production of biogas from waste there was no progress and activity.
14. **Project Status in brief:** There is one work contract under the SWMIP currently being under implementation:

Project activity	Status as per 30 June 2024	Monitoring
CW1-R Sanitary Landfill Establishment	<p>Contract signed between SUE Maxsustrans and JV "STECOL-POWERCHINA GUIYANG" (China) on 31 January 2022.</p> <p>The Contractor was mobilized in March 2022.</p> <p>The Works Commencement Date is 8 April 2022.</p> <p>The scheduled Works Completion Date is 31 July 2024 (as per Contract amendment No. 1).</p> <p>To date the civil works going on.</p>	<p>Social safeguard monitoring covers any social concerns that may occur within the civil works at the new landfill.</p> <p>As no civil works performed on the old dumpsite by Sejin G&E Co., Ltd (Korea) the monitoring has been not conducted in the reporting period.</p>

2. Introduction

15. This report is the 15th Semi-annual Social Safeguard Monitoring Report under SWMIP. The report is prepared to comply with social safeguard requirements of the Government of Uzbekistan and ADB as well as to fulfill the covenants as provided in the Loan Agreement No.: 3067-UZB signed between the Government of Uzbekistan and ADB.
16. The report includes the monitoring and evaluation of social safeguards activities during January – June 2024. The social safeguard monitoring report covers, in particular, the status of social safeguard indicators of SWMIP. The objective of this report is: (i) review overall progress of the project implementation; (ii) identify any social issues and constraints that encountered in project implementation; (iii) develop the social safeguard monitoring indicators for the construction; (iv) recommend mitigation measures (if required). The report describes the status of the social safeguard indicators of the Project during the monitoring period.
17. To conduct the safeguard monitoring under the Project, PIU Consultant currently representing only by Infratech Consulting SDN Ltd. (Uzbekistan) was selected through the international competitive bidding in 2016, and the contract for provision of the consultancy services was signed on 11 January 2017 with the service duration until 31 December 2024 as per amendments to the Contract.
18. Design and supervision on construction of the new sanitary landfill is provided by China Urban Construction Design & Research Institute Co., Ltd. (CUCD) based on the Contract Cons_2 from 16 November 2018 (the Supervision Consultant). The design services of CUCD have been completed in 2019 and the supervision services started in May 2022 and as per Amendment No. 3 to the Contract was ended on 31 October 2023. As the new landfill construction was extended until 31 July 2024, the service period of the Supervision Consultant was agreed to extend from 31 October 2023 at least until 30 September 2024 through Amendment No. 4.
19. After the engineering design for landfill construction is approved, Maxsustrans has launched the international bid CW1-R: Sanitary Landfill Establishment and Dump Site Closure in October 2019. The package was rebid in October 2021 due to excluding the dumpsite closure works from the Project upon decision of the GoU. In November 2021, the rebid has been launched and in January 2022 the Works contract has been signed with JV “Stecol-POWERCHINA GUIYANG” (China). The works commenced on 8 April 2022 and shall be completed on 30 September 2023 (after amendment on 31 July 2024). The Supervision Consultant (CUCD) acts as the Engineer under the contract CW1-R with duration of services until 30 September 2024.
20. Initial project document for social safeguard monitoring is Land Acquisition and Resettlement Plan (LARP) prepared in 2012 for the new landfill construction. Due Diligence for involuntary resettlement impacts was carried out within the project and completed in October 2019. Due Diligence confirmed that the project will not require land acquisition and involuntary resettlement for the landfill construction.
21. The social safeguard monitoring is carried out on semiannual basis. The PIU Consultant also carries out semiannual monitoring to collect information on the status of project implementation and timely response to possible project impacts. The main objective of safeguard monitoring is to provide assessment on social safeguard issues on any negative project potential impacts or any other social concerns that may occur during project implementation.
22. The investment project of the Government of Uzbekistan with the South-Korean company «SEJIN G&E CO., LTD» was approved by the Resolution of the Cabinet of Ministers No. 895

dated November 1, 2018. The project is implemented on the existing dumpsite, which is aimed to biogas producing from waste. The dumpsite project is considered as associated site for ADB project. During the reporting period no construction activities have been recorded on the existing dumpsite.

3. Project Contracts and Management

23. Project management is carried out by the Implementing Agency (IA) - State Unitary Enterprise "Maxsustrans" which is responsible for project administration and implementation (design, construction and operation). A Project Implementation Unit (PIU) is established within SUE Maxsustrans for support in implementation and administration of the SWMIP. The PIU coordinates provision of consulting services, supply of goods and performing the civil works and ensures consistency of work approach and progress reporting. Since December 2023 the PIU is led by acting Head of PIU Mr. Jamoliddin Irbutayev.
24. In accordance with the President's Decree #4925 dated 15.12.2020 "On Improvements of Solid Waste Management of Tashkent city" SUE Maxsustrans is placed under the authority of Tashkent City Municipality (hokimiyat)¹.
25. Since August 2017 PIU Consultant – JV of H.P. Gauff Ingenieure GmbH & Co. KG, GKW Consult GmbH and Eng Invest Consulting Ltd (later renamed Infratech Consulting SDN Ltd.) has started its services. On 24 July 2020 Maxsustrans has received an official letter from H.P. Gauff Ingenieure GmbH & Co. KG. about order of the local court of Nuremberg on opening of insolvency proceedings according to German Law regarding H.P. Gauff Ingenieure GmbH & Co. KG. On 17 September 2020 PIU has received an official letter from H.P. Gauff Ingenieure GmbH & Co. KG about declaration of non-entry of the company in the contract No. SUE/Maxsustrans/QCBS-Cons 1-2016-01.
26. Referring to this, Maxsustrans has amended the Contract Cond_1 and since December 2020 a sole responsibility for the project implementation, safeguard compliance monitoring and progress reporting is taken by local partner of JV - Infratech Consulting SDN Ltd. (the previous name - Eng Invest Consulting Ltd.). Up to date the team of PIU Consultant is managed by the national Deputy Team Leader Mr. Dilshod Mavlyan-Kariev with limited support of international Team Leader Mr. Ingo Schoebe and full support of national experts. The service period of PIU Consultant was extended until 31 December 2024.
27. The Supervision Consultant CUCD after completion of its design services in 2019, in late 2021 has assisted to evaluate the bid proposals of the rebid package CW1-R and to conduct the contract negotiations with the winner company. Since May 2022 the Consultant providing its supervision services, including safeguard monitoring and reporting. On 25 April 2022 the Supervision Consultant has signed Amendment No. 3 to the Contract extending the service period until 31 October 2023 and including changes of key experts and input schedule, reporting requirements etc. The Consultant was remobilized on 5 May 2022 and started the supervision of the works performed by the Contractor – JV "STECOL-POWERCHINA GUIYANG". This Consultant is responsible for supervision over construction of new landfill only. During the reporting period, the Consultant has assisted to Maxsustrans in resolving the design clarification issues and clarification with the Contractor on the drawings and bill of quantities of the Contract No. CW1-R: Sanitary Landfill Establishment.

¹Please refer to Annex 2 of the Uzbekistan President's Decree No. 4925.

28. The Supervision Consultant is responsible for preparing Construction Supervision Progress Reports and Social Safeguard Monitoring Reports on the quarterly basis. The safeguard report shall include briefing supervision of safeguard works and summarizing the results of Contractor's monitoring report and external monitoring report (if any) for the reporting semi-annual report. This task is cancelled by SUE Maxsustrans since April 2023, because it overlaps with the same tasks of PIU and PIU Consultants. The original completion date of the supervision services was 31 October 2023, now the Consultant and SUE Maxsustrans agreed the Amendment No. 4 to the Contract Cons_2 extending the service duration at least until 30 September 2024.
29. The first draft Amendment No. 4 was pre-agreed and signed by the Supervision Consultant in August 2023, i.e. 2 months before ending the service period specified by Amendment No. 3. According to local legislation any amendment to the contracts shall be first approved by local authority and then by ADB. In case of contract amount increasing by more than 15% than original amount the subject shall be also agreed by the Government. Unfortunately, up to date no positive conclusion to the draft Amendment No. 4 has been obtained by the responsive authority and the Government of Uzbekistan. The available draft Amendment No. 4 was agreed with SUE Maxsustrans in February 2024 and the respective Minutes of Meeting was signed by the parties, but up to now these documents are not finalized and signed. The local authority does not agree to allocate the loan funds for financing the rate adjustments of the Consultant's experts, that is allowed by the contract conditions. Since months this strong position of the authority is not changed and it led to delay with signing the amendment No. 4 and outstanding payments of Consultant.
30. Considering the above, the Supervision Consultant sent to the Client an official letter No. 64 dated 1 June 2024 informing the service suspension from 3 June 2024 until an official positive feedback on Amendment 4 from the authority and Government of Uzbekistan is obtained. So, since 3 June 2024 the whole team of the Supervision Consultant including local sub-consultants has stopped any activities and services in the new landfill project.
31. Since the construction works of CW1-R commenced in April 2022, the Social Safeguard Specialist of the Supervision Consultant was responsible for monitoring of implementation of the Social Action Plan and Gender Action Plan (incl. Resettlement Plan) by the Contractor and regularly reporting to PIU and Maxsustrans on compliance with the social safeguard requirements of the Project. This task was performed until April 2023 and then cancelled by the Employer due to overlapping this task with the social safeguard expert of PIU Consultant. PIU Consultant is responsible for overall monitoring of the Supervision Consultant and the Contractor CW1 with regard to their compliance on social safeguard and reporting.
32. The construction works under the Contract CW2: Transfer Station Rehabilitation and ended by 31 August 2022. The works have been commissioned in September 2022 by the Engineer – the Supervision Consultant (Quality Planning Ltd., UZB) and the Employer (SUE Maxsustrans). The rehabilitated transfer stations are operation since September 2022, the Performance Certificate has been issued by the Engineer in December 2023 – after remediation of the identified defects in the both transfer stations. These transfer stations located on the land allocated for SUE Maxsustrans, therefore no land extension or acquisition was foreseen according to the final design, no social issues and constraints have been identified during the construction period, which shall be monitored by the Consultant.

4. Social Safeguard Activities during January – June 2024

4.1 Objectives of the report and methodology

33. The objectives of the social safeguard monitoring within the monitoring period of January – June 2024 were to:
- review overall progress of the project implementation;
 - identify any social issues and constraints that encountered in project implementation;
 - monitor the social safeguard indicators during the construction phase under CW1-R;
 - assess of potential impacts of the waste to energy project of SEJIN G&E CO., LTD;
 - recommend the mitigation measures (if required).
34. Monitoring and evaluation is directed to confirm that the project implementation does not trigger ADB's Safeguard Policy Statement (2009)'s Safeguard Requirements.

4.2 Scope of Social Safeguard Monitoring Report

35. This report was prepared by the PIU Consultant according to the contractual Terms of Reference in order to ensure the compliancy to ADB's safeguard policy and to conduct the semi-annual monitoring to assess any various phenomena that may lead to preconditions for the construction and during the construction of the new landfill, as well as any measurement standards for the consideration of consequences, respectively.
36. The report includes developed monitoring indicators for the construction period to minimize any social impacts related to the construction site.

4.3 Project activities in January – June 2024

37. No construction or other activities were observed on the old dumpsite by the South Korean company SEJIN G&E CO., LTD during the reporting period.
38. A loan review mission was fielded from 27 to 31 May 2024. Maxsustrans assured the Mission no pending land acquisition and resettlement issue, ADB SPS 2009 requirements are compliant with, as well as applicable laws and regulations of Uzbekistan, compensation and provide other resettlements entitlements before physical or economic displacement for affected person. In the last March 2023 mission, the Mission was informed on the minor change in the access road alignment which will be provided from the government reserved land. The final design of the access road had been approved by the state expertise in September 2023 and civil works are underway.

4.4 Project monitoring for the construction period

39. The Consultant developed the indicators for conducting social safeguard monitoring during the construction phase. The requirements for social safety at the construction site are included in the scope of works of the Contractor. The Contractor considers implementation and monitoring of the following social and gender issues and the Consultant monitors, but not limited, the following indicators:

Table 1 Social safeguard monitoring indicators for construction stage of the package CW1-R

Stage	Monitoring indicator	Mitigation measures	Responsible entities
Community Impacts	Community health, safety and security	<ul style="list-style-type: none"> Development and implementation of procedures for protecting public health and safety will be provided; Ensure safety for the population during the movement of vehicles. Set the minimum vehicle speed for the project site and nearby roads; Establish fences and warning signs for the residents in order to avoid accidents and harm to human health; Work on the construction site will not be carried out during rest time and at night; Sound absorbing installations at the construction site should be installed to reduce noise / vibration from the operation of the equipment. Necessary measures to prevent the spread of infectious diseases among the population should be taken. 	Contractor, Sanitary Landfill Design and Supervision Consultant and Social safeguard specialist of PIU Consultant to monitor
	Lands	<ul style="list-style-type: none"> Land plots are allocated for the project from the reserve fund of the Tashkent Region Administration (Khokimiyat). No additional land plots will be required for the project construction; All construction works should be carried out within the allocated land; Storage of building materials in the territory of used agricultural land plots is not allowed; Storage of construction materials and their disposal in places of location of irrigation canals for crops irrigation is not allowed. 	Contractor, Sanitary Landfill Design and Supervision Consultant and Social safeguard specialist of PIU Consultant to monitor

Stage	Monitoring indicator	Mitigation measures	Responsible entities
	Losses of agricultural crops	<ul style="list-style-type: none"> The entry and exit of vehicles and equipment at the construction site should be under strict control. Traffic on the construction site should be carried out only within the existing roads. Entry of vehicles on the area of used agricultural land is not allowed. Properly regulation of the delivery and storage of materials to the project site should be provided; Regular monitoring to ensure that any impacts on agricultural land and crops are minimized and compensated in a timely manner (if necessary) should be carried out. 	Contractor, Sanitary Landfill Design and Supervision Consultant and Social safeguard specialist of PIU Consultant to monitor
	Income losses	<ul style="list-style-type: none"> Regular monitoring will be carried out to assess the impact of the project on the population. If the monitoring reveals the impact on the incomes of the population living / working near the construction site caused by the project implementation, an impact assessment will be carried out and measures will be developed to address it. 	Contractor, Sanitary Landfill Design and Supervision Consultant and Social safeguard specialist of PIU Consultant to monitor
	Local economic and employment	<ul style="list-style-type: none"> Employment during the construction period as much as possible of the local population in order to increase employment and income. Provision of job opportunities for local residents, low-income people and women. 	Contractor, Sanitary Landfill Design and Supervision Consultant and Social safeguard specialist of PIU Consultant to monitor
	Existing social infrastructure and services	<ul style="list-style-type: none"> Construction site is located in the sanitary protection zone and is removed from the social infrastructure; Transport machinery, equipment, transportation and storage of building materials should not limit the access of the population to roads, driveways, canals and any other social facilities. 	Contractor, Sanitary Landfill Design and Supervision Consultant and Social safeguard specialist of PIU Consultant to monitor
	Public meetings and consultations	<ul style="list-style-type: none"> Inform the population and all interested persons and organizations about the current situation of the project. Hold as necessary public meetings with the population of communities nearby to the construction site. 	Contractor, Sanitary Landfill Design and Supervision Consultant and Social safeguard specialist of PIU Consultant to monitor


Stage	Monitoring indicator	Mitigation measures	Responsible entities
Construction site	Occupational health and safety	<ul style="list-style-type: none"> • Complying with ADB labor standards and national labor laws; • Introduction and operation meetings should be undertaken by all workers. • The entry and exit of vehicles and equipment at the construction site should be under strict control. Traffic on the construction site should be carried out only within the existing roads. Speed limits will be used for traffic safety. • HSE manuals and require placement of safety signs and placards. • Safety for the population during the movement of vehicles will be provided. • Fences and warning signs for the residents in order to avoid accidents and harm to human health will be established; • Work on the construction site will not be carried out during rest time and at night; • Sound absorbing installations at the construction site will be installed to reduce noise / vibration from the operation of the equipment. • Only qualified workers will be hired. Strictly impose and monitor use of PPE by workers. Regular inspections will be conducted. • Equal working conditions for men and women should be provided; • Properly regulation of the delivery and storage of materials to the project site should be provided; • Awareness and training programs on safety and health issues will be conducted by the designated HSE Officer. Regular worksite safety trainings for all workers. Proper records of trainings; • Provision of necessary hygiene facilities for all workers at the worksite, including appropriate and adequate facilities for women workers; • Conducting trainings on communicable diseases and HIV/ AIDS for all workers as well as nearby communities. Proper records of trainings; • Registration of any complaints raised by local residents or workers at the worksite. 	Contractor, Sanitary Landfill Design and Supervision Consultant and Social safeguard specialist of PIU Consultant to monitor

5. Redress Grievances

40. A project-specific grievance redress mechanism (GRM) is established by the EA to provide a transparent mechanism to voice and resolve environmental concerns linked to the project. According to the Decree of President of the Republic of Uzbekistan SUE Maxsustrans established “People’s Reception Room” in its each district branch in Tashkent city, including one in SUE Maxsustrans building for PIU related queries. The EA ensures that grievances and complaints are addressed in a timely and satisfactory manner to avoid any potential delays in the establishment of the project.

Figure below gives the details of the grievance redress mechanism.

Figure1 Grievance Redress Mechanism*

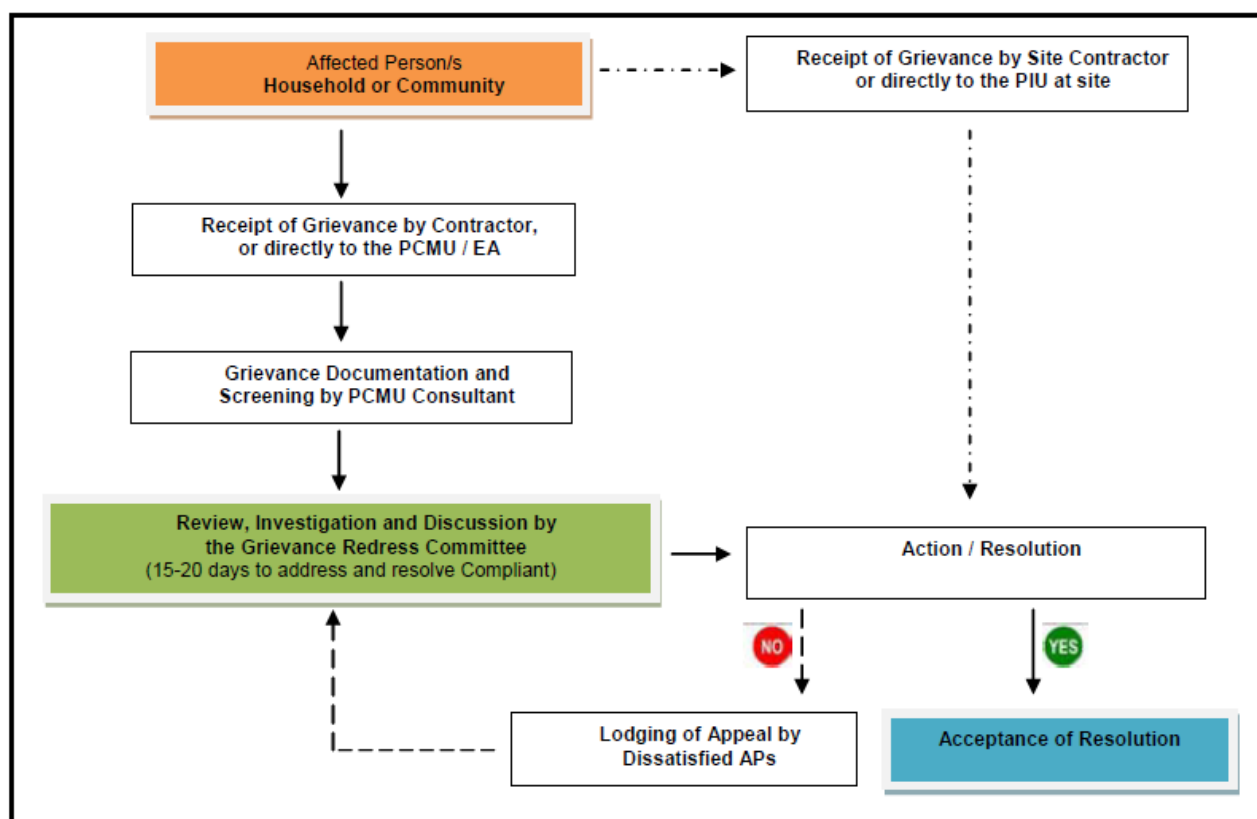


* PIU – responsible person for GRM is the acting head of PIU, Mr. Jamoliddin Irbutayev, tel: +998 712473816, email: piu3067@gmail.com; PIU Consultant's Deputy Team Leader, Mr. Dilshod Mavlyan-Kariev, tel: +998 712477923, email: dilshod75@mail.ru

41. The PIU has established Grievance Redress Committee (GRC). GRC provides any APs a venue to file complaints and queries on any environmental (or social) aspect related to the project. Grievances can be submitted in writing or orally to the contractor or directly to the PIU / EA contact person. These are properly documented (i.e. indicating the date it was received, details of the complaint and complainant/s) and screened by the designated PCMU safeguard consultant for its veracity and validity. The committee has 15 to 20 days to address and come up with a resolution. Under this GRM, unsatisfied grievances may be able to appeal for a final resolution. This mechanism also does not prevent any AP to approach regulatory agencies to assist and resolve complaints at any stage of the process. In occasions wherein grievances are perceived by the AP to be immediate and urgent; the contractor, EHS officer and PIU on-site supervisor will provide the most accessible and practical solution for a quick resolution of grievances. Such grievances and respective resolutions submitted to the PIU for proper documentation. The PIU contact person is responsible for recording the complaint, the step

taken to address grievance, minute of the meetings and preparation of a report for each complaint. Records is kept by the PIU of all grievances received including contact details of AP, date the complaint waste received, nature of grievance, agreed remedial / corrective action and the date this was implemented, and the final outcome in Complaints Log Book kept at the PIU office.

42. Together with the contractor's specialists, the experience of grievance work has been reviewed. A grievance redresses log has been maintained. A poster on grievance redress mechanism has been prepared and posted at the construction site with phone numbers to contact. Complaints and suggestion boxes were also placed at the landfill and nearby.

Figure 2 – “Grievance redress scheme” poster

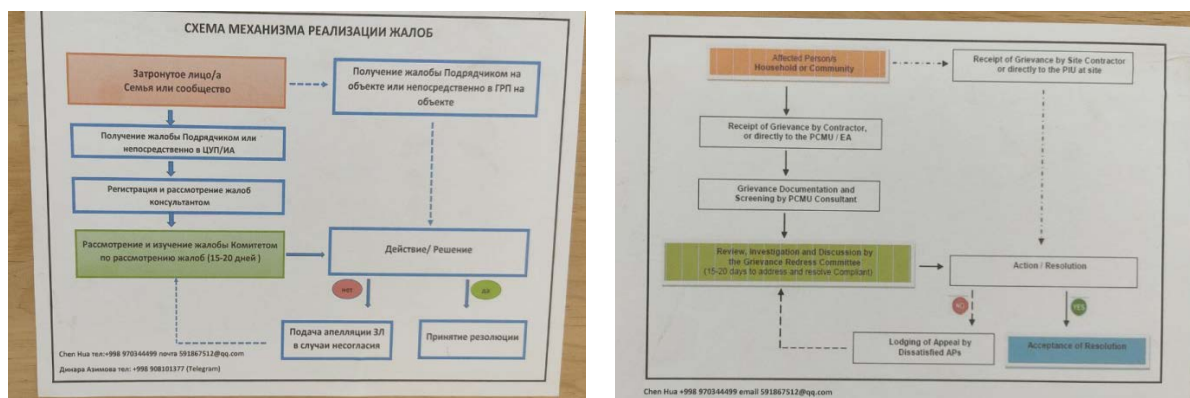

43. The complaint handling process will be reported to ADB through monitoring reports. The PIU safeguard consultant will periodically review and record the efficiency and effectiveness of the GRM highlighting the project's ability to prevent and address grievances.
44. In period of January - June 2024 the Social Safeguard and Development Specialist of the PIU Consultant contacted with the representatives of Regional and District Hokimiyat of the project area to obtain information on complaints. No complaints/addresses are received during the monitoring period. The Consultant will continue monitoring of complains under the Project at further stage of project implementation and construction works to ensure the proper and timely address any complains under the project.

6. Public Awareness and Consultations

45. During the monitoring period, the Consultant did not conduct public consultations on the Project issues. In the first half of 2024, no complaints were received during the implementation of the project.
46. The management of SUE Maxsustrans was invited to public consultations and regularly information in the Parliament of Tashkent City to inform about performance of the company and activities under ADB project within the last 12 months and necessity to increase the fleet of the company in order to provide the waste collection services in the extended areas of Tashkent city. The working group of the City Parliament has requested to present the operational and financial performance results of Maxsustrans as well as the key achievements at upgrading the solid waste management system of Tashkent city financed by ADB loan.



7. Conclusions

48. The construction works under the Contract CW1-R: Sanitary Landfill Establishment going on and the Contractor implements the safeguard measures, including regular reporting. According to the amended contract the Contractor covers the cost of compliance with the Social Development and Gender Action Plan (SAP/GAP), including the Resettlement Plan until the extended construction period – 31 July 2024.
49. There is no construction activity on the old dumpsite located in Akhangaran district (59 ha), because of cancellation of this work component from the Project.
50. The consulting services during the construction supervision phase on the new landfill site are being provided by the PIU Consultant and the Supervision Consultant and the safeguard monitoring and reporting tasks are performed based on the task distribution matrix agree with the Consultant and other stakeholders of the Project in June 2023.
